

Pittsburg Unified School District



CONSTRUCTION
UPDATE

FACILITIES PLANNING
& MANAGEMENT

April 5, 2018

Construction Status Update

2

- Construction @ Willow Cove ES, Bldg. E (former MP/Cafeteria Bldg.) is continuing. Photos show progress since the last Report dated 03/23/18. Anticipated completion date is on or before 04/30/18.
- Demolition @ Bldg. D (former Library Bldg.) has started for remodeling. Anticipated completion date is on or before 06/30/18.
- Contractor is finishing with Punchlist Items Work @ the New Gym./MP Bldg. Project and @ the HVAC & Roofing Project @ the Existing School Bldgs. All Punchlist work to be completed by 04/30/18.
- Bid Opening took place on Wednesday, March 28, 2018 for Foothill Elementary School and Highlands Elementary School Play Structure Replacement Project. Three Bids were received: (1) Community Playground, Inc. @ \$349,000.00; (2) Greentech Industry, Inc. @ \$395,000.00 and (3) Pacific Coast General Engineering, Inc. @ \$425,911.00. Staff recommends that Community Playground, Inc. be granted Contract Award to perform on the play structure replacement work for this Project.
- Bid Opening took place on Wednesday, March 28, 2018 for Pittsburg High School Gymnasium Buildings Lighting Retrofit Project. Only one Bid was received. It was from Pacific Metro Electric, Inc. @ \$282,771.00. Staff recommends that Pacific Metro Electric, Inc. be granted the Award to perform work for the Pittsburg High School Gymnasium Buildings Lighting Retrofit Project.

WILLOW COVE ELEMENTARY SCHOOL

3



View of Modernization Work @ Building E - Looking North toward Computer Lab. Window wall had been framed & sheetrock was installed. Taping in Progress.

WILLOW COVE ELEMENTARY SCHOOL

4



View of Modernization Work @ Building E - Looking Northeast toward Hallway & Book Storage Room. Sheetrock was installed.

WILLOW COVE ELEMENTARY SCHOOL

5



View of South Wall of New Library from Computer Lab., @ Building E. Sheetrock completed. Taping in progress.

WILLOW COVE ELEMENTARY SCHOOL

6



View of Reading Nook Stadium Seating @ Building E – Looking Southwest. Handrails installed & sheetrock finished. Taping in progress

WILLOW COVE ELEMENTARY SCHOOL


7



View of Modernization Work Inside of New Book Storage Room @ Building E.

WILLOW COVE ELEMENTARY SCHOOL

8

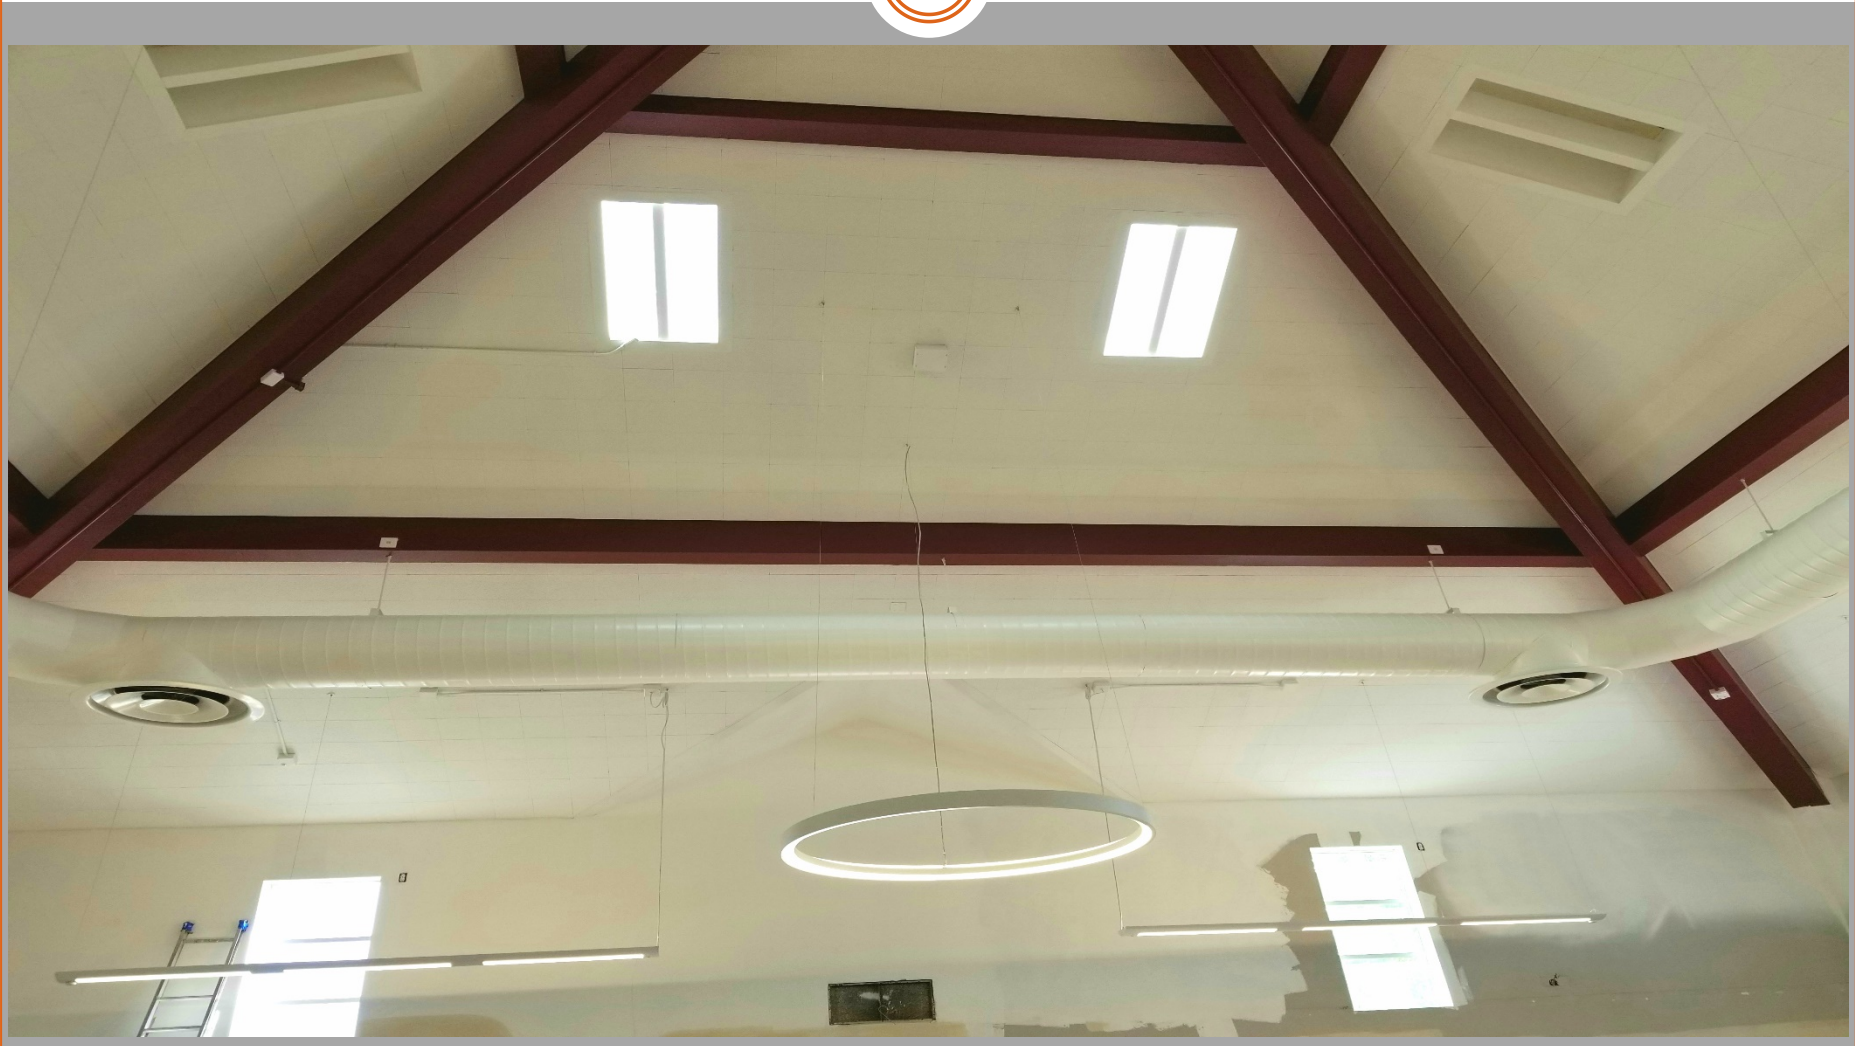

Viewing South Slope Ceiling @ Building E - Skylights Installed, Ductwork Beams and Ceiling were painted.

WILLOW COVE ELEMENTARY SCHOOL

9



Viewing the Old Library. Demolition has started for remodeling of Building D.
