



Pittsburg Unified School District

1

CONSTRUCTION UPDATE

FACILITIES PLANNING
& MANAGEMENT

July 13, 2018



Construction Status Update

2

- Willow Cove New MPR and Modernization Project. Construction @ Willow Cove ES, Building E (former MP/Cafeteria Bldg.) and remodeling @ Building D (former Library Bldg.) are on final stage of completion. Photos show progress since the last report dated July 6. Punchlist items and door installation should be completed by July 30. Period of Performance Completion date is extended to July 30th.
- Play Structures Replacement Project at Foothill ES and Highlands ES. Photos show progress since the last report. Play structures equipment has been installed. Concrete pour on both sites are completed. Projected completion date is August 10th.
- Pittsburg High School Gym Buildings Lighting Retrofit on the Big Gym. Building 14 Gym Lighting Complete (Gym can be occupied). Gym Lighting Controls – Complete (Programming, Commissioning and Training Scheduled week of 07-23-2018). Building 15 Gym Lighting – Gym Lighting (Scheduled to be Completed week of 07-23-2018). Building 16 Gym Lighting - Complete (Gym can be occupied). Gym Lighting EM Batteries – EM Batteries (Scheduled to be Completed 07-17-2018 thru 07-20-2018) Gym Lighting Controls – Complete. Final Punchlist to be Scheduled week of 07-30-2018. Projected completion date is August 31st. Project is currently ahead of schedule.
- SSSC Bioswale Integrated Energy System Project. Equipment Delivery of Solar Racks, Modules and Wind Turbines (Scheduled to be delivered 08-06-2018 thru 08-24-2018). Equipment Installation Scheduled to be Completed 08-06-2018 thru 09-21-2018. Start Up and Commissioning (Scheduled to be Completed week of 09-24-2018). Projected Completion date is September 30th. This project is currently ahead of schedule.

WILLOW COVE ELEMENTARY SCHOOL

3



Willow Cove ES - Building E New Bathroom Doors Installation, in progress.

WILLOW COVE ELEMENTARY SCHOOL

4



Willow Cove ES Modernization Work @ Building D Frames for Glass arrived for New Doors.

PITTSBURGH HIGH SCHOOL


5



PHS Gym Buildings Lighting Retrofit. Main/Big Gym – New Lights installed.

PITTSBURGH HIGH SCHOOL

6

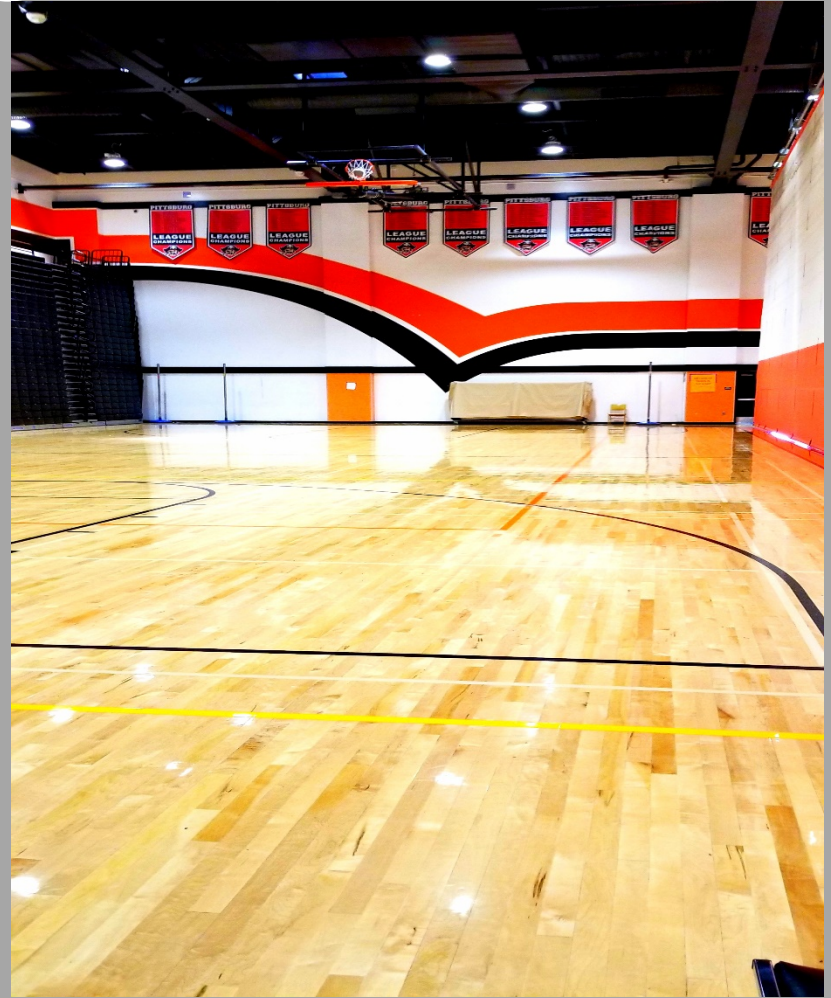

PHS Gym Buildings Lighting Retrofit. Main Gym - Bright, well-lit floors.

PITTSBURGH HIGH SCHOOL

7



PHS Gym Buildings Lighting Retrofit. Wrestling Gym - Lights installed.

HIGHLANDS ELEMENTARY SCHOOL

8



Highlands ES New Play Structure – Concrete Pour Done.

HIGHLANDS ELEMENTARY SCHOOL

9



Highlands ES New Play Structure different angle.
